Name Of Work : Providing and laying HDPE Water line in Ganesha Temple Block-1 in J P Park Ward No-17.							
A) Detailed Measurements							
Item No	**Discription of Item**	**No**	**Length**	**Breadth**	**Depth**	**Qty**	**Unit**
22	Conveying the excavated earth silt debri\s and over burden earth etc., to a lead of upto 9 to 10km distance by using private vehicle this includes the cost of loading and unloading charges etc complete.						
	Quantity Vide Item No:1					1404.75	
	Quantity Vide Item No:14					505.35	
	Quantity Vide Item No:1 - Quantity Vide Item No:14					899.40	
					Present Qty	**899.40**	**Cum**

Certificate:

1 This is to certify that work done is satisfactorily.
2 There is no departmental issues of material by BBMP.
3 All the debris have been cleared from the work spots by agency.

7/5

7/5

Asst. Executive Engineer
Yeshwanthpura Sub-Division
Bruhat Bangalore Mahanagara Palike

Asst. Executive Engineer
Yeshwanthpura Sub-Division
Bruhat Bangalore Mahanagara Palike

NAME OF WORK :- PROVIDING AND LAYING HDPE WATER LINE IN GANESHA TEMPLE BLOCK-1 IN J.P. PARK WARD NO 17.

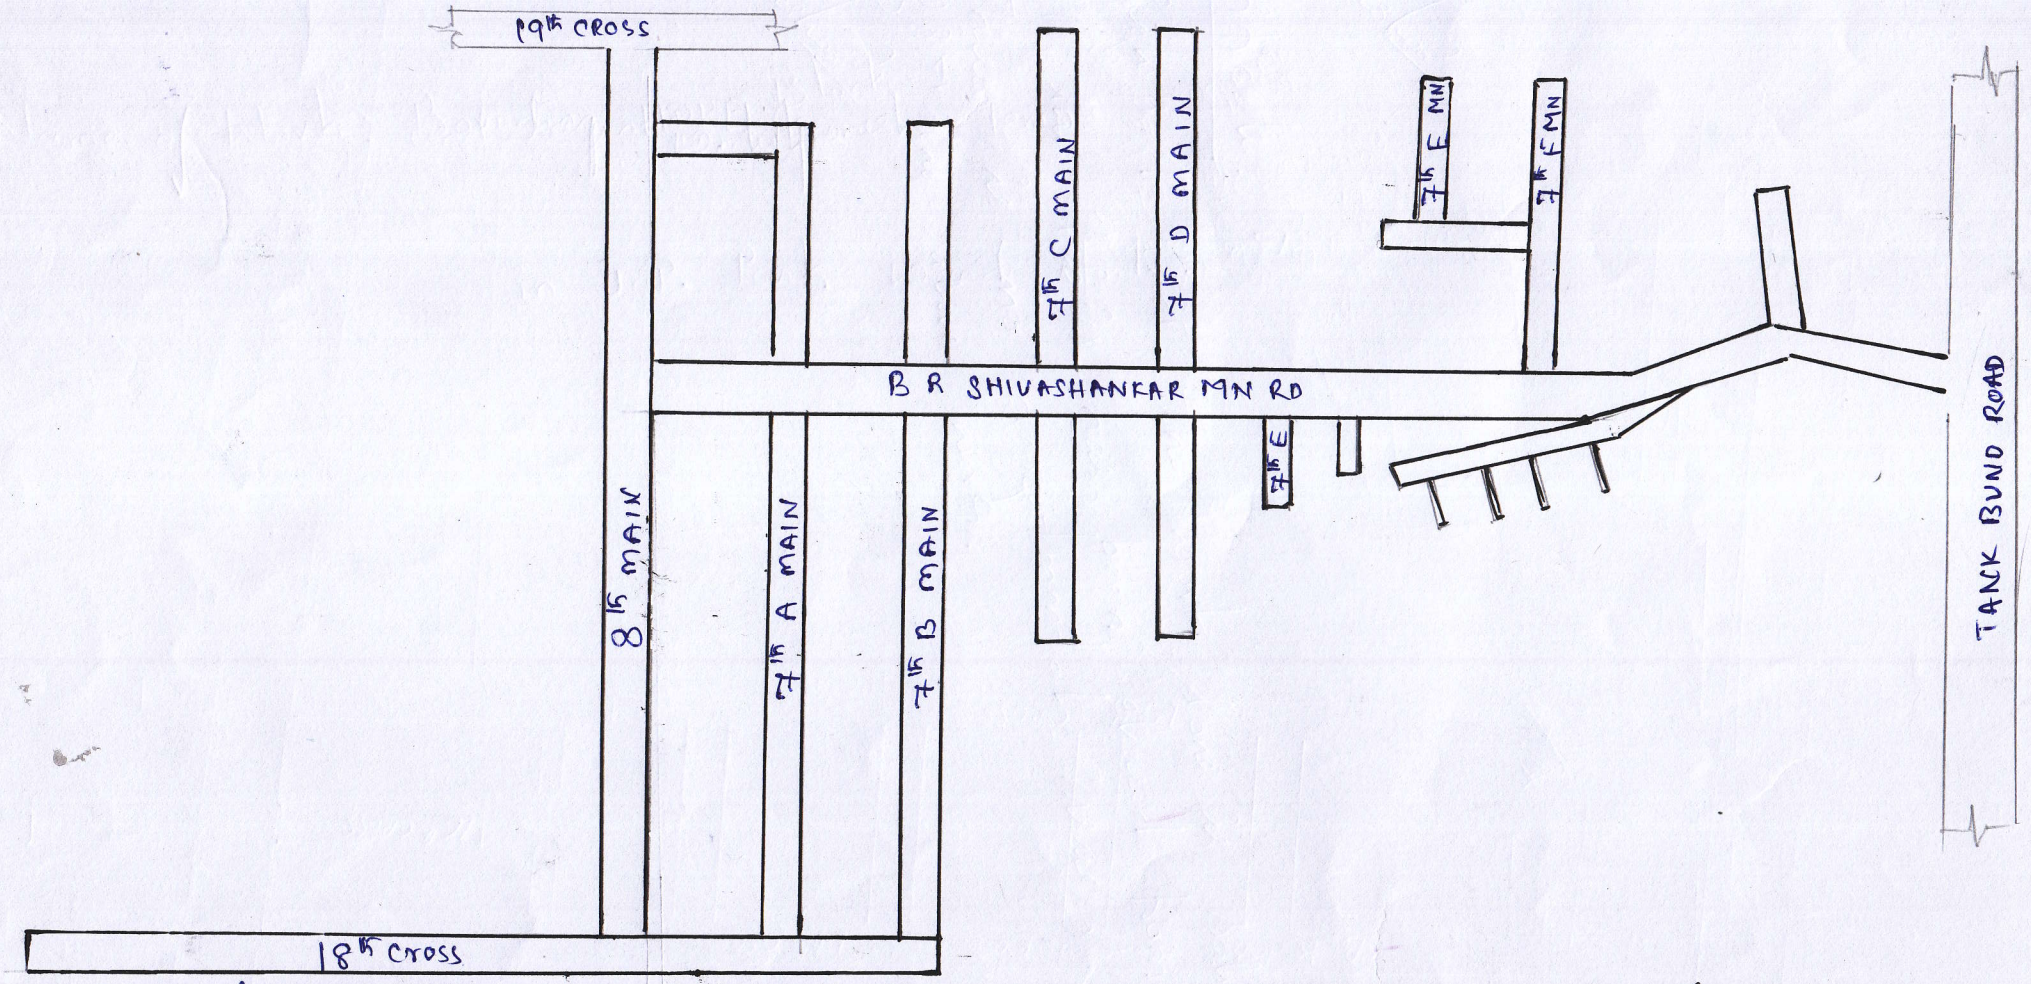

Asst. Executive Engineer
Yeshwanthpura Sub-Division
Bruhat Bangalore Mahanagara Palike

Executive Engineer
Rajarajeshwarinagar Division
Bruhat Bangalore Mahanagara Palike

ABSTRACT OF BILL -1st and Final Bill

Name Of Work : Providing and laying HDPE Water line in Ganesha Temple Block-1 in J P Park Ward No-17.

Sl. No	Description of Item	Unit	As per Schedule B			Previous Measurements			Present Measurements			Total upto date	
			Qty	Rate	Amount	Qty	Rate	Amount	Qty	Rate	Amount	Qty	Amount
1	KSRB 2-2.2 : Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 0.6.5m and above in width, in hard soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods complete as per specifications.	Cum	2289.60	244.00	558662.40	-	-	-	1404.75	244.00	342758.27	1404.75	342758.27
2	KSRB13-9.3 : Providing and fixing to wall, ceiling and floor high density polyethylene pipes 6.00 kgf/sq.cm working pressure 50mm outside diameter with special flange, compression type fittings, wall clips, making good the wall, ceiling and floor, including cost of all materials, labour charges, HOM of equipments and testing complete as per specifications. Specification No.KBS 13.2.15.2 / 13.9	Rmt	2198.00	536.00	1178128.00	-	-	-	2290.00	536.00			
	Limit to Tender Qty					-	-	-	2198.00	536.00	1178128.00	2198.00	1178128.00
3	KSRB13-10.3 : Providing and fixing to wall, ceiling and floor HDPE pipes 10.00 kgf/sq.cm working pressure 25mm outside diameter chemp plast / Wavin or equivalent make with pipe fittings, wall clips, making good the wall, ceiling and floor, including cost of all materials, labour charges, HOM of equipments and testing complete as per specifications.	Cum	2925.00	114.00	333450.00	-	-	-	2925.00	114.00	333450.00	2925.00	333450.00

Sl. No	Description of Item	Unit	As per Schedule B			Previous Measurements			Present Measurements			Total upto date	
			Qty	Rate	Amount	Qty	Rate	Amount	Qty	Rate	Amount	Qty	Amount
4	KSRB13-3.2 : Providing and fixing in trenches galvanised / mild steel tubes (medium grade) 20mm dia nominal bore with all fittings (earth work in trenches to be measured and paid for separately) including cost of all materials, labour charges, HOM of equipments and testing complete as per specifications.	Rmt	468.00	211.00	98748.00	-	-	-	-	-	-	-	-
5	Providing and fixing 25mm dia nipple,complete as per specification.	No	390.00	34.00	13260.00	-	-	-	390.00	34.00	13260.00	390.00	13260.00
6	Providing and fixing reducer elbow 25mm to 20mm complete as per specification.	No	780.00	44.00	34320.00	-	-	-	780.00	44.00	34320.00	780.00	34320.00
7	Providing and fixing 20mm dia nipple,complete as per specification.	No	390.00	22.00	8580.00	-	-	-	390.00	22.00	8580.00	390.00	8580.00
8	Providing and fixing HDPE 90X32m Saddle with brass nuts and bolts including cost of all materials, labour charges,HOM of equipments and testing excluding cost of fittings,comple as per specification	No	780.00	375.00	292500.00	-	-	-	780.00	375.00	292500.00	780.00	292500.00
9	Providing and fixing 20mm dia union,complete as per specification.	No	390.00	58.00	22620.00	-	-	-	390.00	58.00	22620.00	390.00	22620.00
10	Providing and fixing 20mm dia union,complete as per specification.	No	780.00	28.00	21840.00	-	-	-	780.00	28.00	21840.00	780.00	21840.00
11	Providing and fixing reducer 20mm elbow complete as per specification.	No	780.00	19.00	14820.00	-	-	-	780.00	19.00	14820.00	780.00	14820.00
12	Providing and fixing reducer 20mm to 15mm reducer elbow, complete as per specification.	No	780.00	24.00	18720.00	-	-	-	780.00	24.00	18720.00	780.00	18720.00
13	Providing and fixing 20mm NP bib cock complete as per specifications.	No	390.00	202.00	78780.00	-	-	-	390.00	202.00	78780.00	390.00	78780.00
14	KSRB 2-4 : Refilling available earth around pipe lines, cables in layers not exceeding 20cms in depth, compacting each deposited layer by ramming after watering with lead upto 50m. and lift upto 1.5 m. including cost of all labour complete as per specifications.	Cum	3596.00	65.00	233740.00	-	-	-	505.35	65.00	32847.46	505.35	32847.46
